

# Beach + Canal Container Villas

Master project document — V2 / V3 two-level container homes

Moonlight Bay de Consejo · Corozal District, Belize · display units targeted at canal lots #207 / #208

This master binds two documents into one working reference:

- 1. Front matter (this section) — how to use the document, open-item register, site & orientation findings, footprint options, supplier & landed-cost tooling.
- 2. Schematic architectural package, Rev 01 (07 Sep 2026) — 14 sheets G001–G004, A101–A501, S001, B001, reproduced unaltered.

*Where the front matter and the schematic package differ, the schematic package governs on all engineering and architectural content; the front matter governs on site orientation, covenant fit, procurement, and landed cost. Nothing here authorizes container cutting, steel procurement, or construction.*

How to use this document

This is the single reference the owner, factory suppliers, and the local architect/engineer all work from. Read the front matter first — it frames what is decided, what is assumed, and what must still be verified — then the schematic sheets in order.

Roles

- **Owner:** resolve the priority-1 open items (survey, covenant text, flood data). Choose V2 or V3. Approve palette and budget.
- **Factory suppliers (×2):** quote V2 base, V3 increment, and site alternates separately (Sheet B001). Return coordinated shop drawings + calcs.
- **Local architect / engineer:** develop and approve the site-specific construction set. Own foundation, flood, structural load path, covenant compliance.

Status legend

- **Decided** — module base (4× 40ft HC), two-level V2/V3 strategy, general look.
- **Assumed** — lot orientation, lot dimensions, covenant minimum (1,000 sq ft). Verify before layout freeze.
- **Open** — survey, flood datum, foundation, exact steel, certified usable area, utility specs (see register, next page).

Document map

| Section               | Sheets     | Content                                                                                                  |
|-----------------------|------------|----------------------------------------------------------------------------------------------------------|
| Front matter          | F1–F5      | Cover, how-to, open-item register, site/orientation findings, footprint options, supplier + cost tooling |
| Design brief & basis  | G001–G004  | Design direction, dimensional control, siting strategy, source register                                  |
| Floor plans           | A101–A202  | V2 lower/upper, V3 lower/upper — dimensioned schematic                                                   |
| Elevations & section  | A301–A401  | Beach/canal & side elevations; transverse section, load path, stair                                      |
| Structural & openings | S001, A501 | Factory structural-coordination map; openings/door schedule                                              |
| Factory scope         | B001       | Quotation scope, three priced figures, return package                                                    |

The schematic package's own "CONCEPT ONLY" stamps, dimensional cautions, and source register remain in force on every one of its sheets.

Open-item register — first coordination-meeting agenda


Consolidated from Sheet G004 plus the site/cost findings in this front matter. Priority 1 items gate the layout freeze.

| Pri | Open item / decision                                                                                          | Owner                   | Status             |
|-----|---------------------------------------------------------------------------------------------------------------|-------------------------|--------------------|
| 1   | Survey of #207/#208: boundaries, setbacks, easements, exact canal & road sides                                | Owner + surveyor        | Open               |
| 1   | Covenant text: minimum floor-area definition, stories/height, exterior restrictions                           | Owner + local architect | Open               |
| 1   | Flood / surge / wave criteria, freeboard, geotechnical & scour data                                           | Local engineer          | Open               |
| 1   | Orientation: 207/208 are canal-front + interior (NOT beach-to-canal). Rotate or corner-glaze — see Finding F4 | Owner + local architect | Flagged            |
| 1   | Container system: true 40ft HC conversions vs. factory module dimensions                                      | Factory                 | Open               |
| 2   | Choose V2 (2-bed) or V3 (3-bed). 4-module clears 1,000 sq ft; 3-module (960) does not                         | Owner                   | Confirmed 4-module |
| 2   | Occupancy: private vs rental/resort — accessibility & fire basis                                              | Owner + local architect | Open               |
| 2   | Utility voltage/frequency, water/sewer, HVAC, hot-water equipment                                             | Factory + local MEP     | Open               |
| 2   | Customs: HS 9406.20 (steel modular) — confirm Belize duty/GST with broker; DDP to 240-A Bayview Dr            | Owner + broker          | Flagged            |
| 3   | Material palette, glazing supplier, coating warranty, budget, delivery programme                              | Owner + factory         | Open               |

## Finding F4 — #207/#208 orientation (resolves open item G003)

The schematic package (Sheet G003) assumes beach and canal lie at opposite short ends and warns: "if the water views are adjacent, rotate the home." The Moonlight Bay lot tracker shows #207/#208 are canal-front and interior lots beside the Boat Basin — canal on one long side; internal road and neighbors on the others. They are not between the beach and the canal (the beach is the far-east sea row, lots 188–202). The design must rotate so a long glazed elevation faces the canal, or develop corner glazing after structural review — do not mirror blindly.

### Envelope-fit reconciliation: architect package vs. actual #207 / #208 orientation

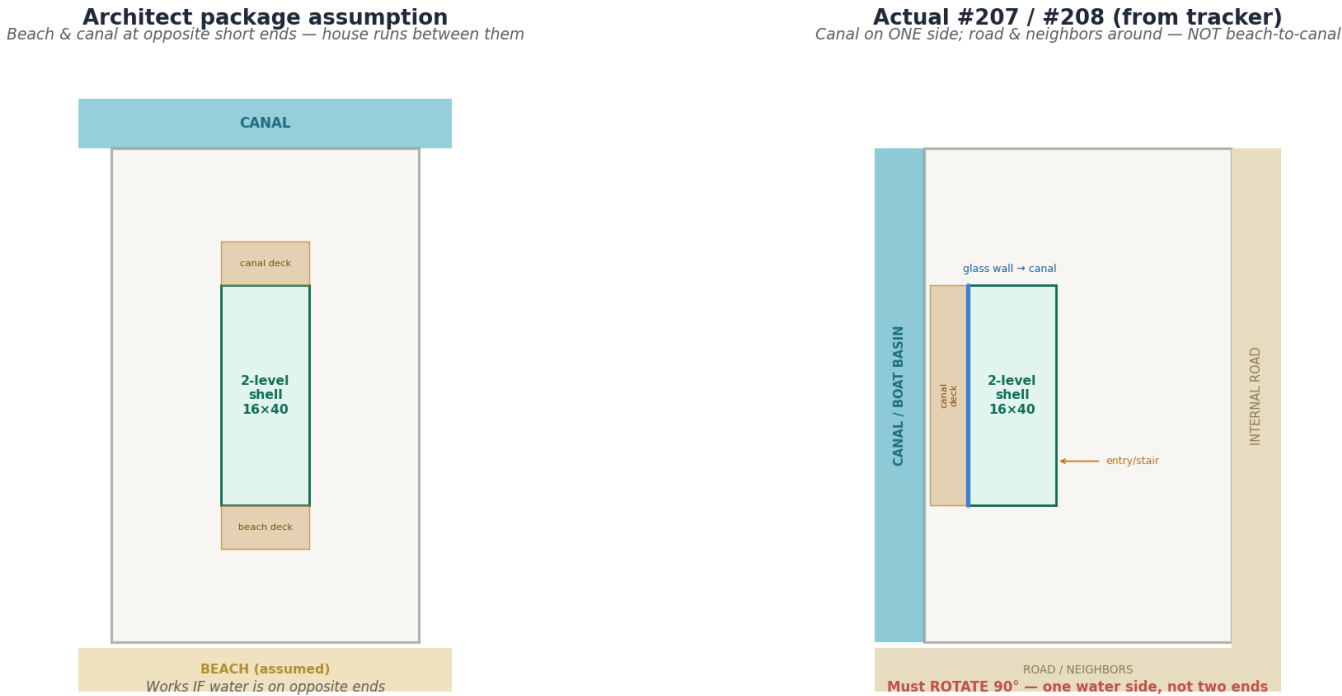

Architect shell 4,876 × 12,192 mm (16 × 40 ft); deck-to-deck 4,876 × 16,392 mm (16 × 54 ft). Fits a ~55×90 ft lot easily on size — the issue is orientation. #207/#208 are canal-front + interior, not beach-to-canal. Confirm exact lot dimensions by survey before freezing.


Consequences: the beach-facing 2,400mm deck loses its rationale on these lots; the canal deck/balcony becomes the primary outdoor space. SG1/SG2 glazing placement and the entry/stair side must be re-resolved for a one-water-side lot. This is a design decision for the local architect, to be settled before layout freeze.

## Footprint options & procurement tooling


The four-module two-level villa (Option B/C below) is the design that both matches the desired look and clears a 1,000 sq ft covenant minimum (~1,057 sq ft net per Sheet G002). The 3-container / 960 sq ft option is retained only for contexts with no 1,000 sq ft minimum.

### Container-home footprint options on a canal lot (#207 / #208)


**Option A — 3 × 40ft, single level**  
960 sq ft · 3 bed / 2 bath · 24' × 40' footprint

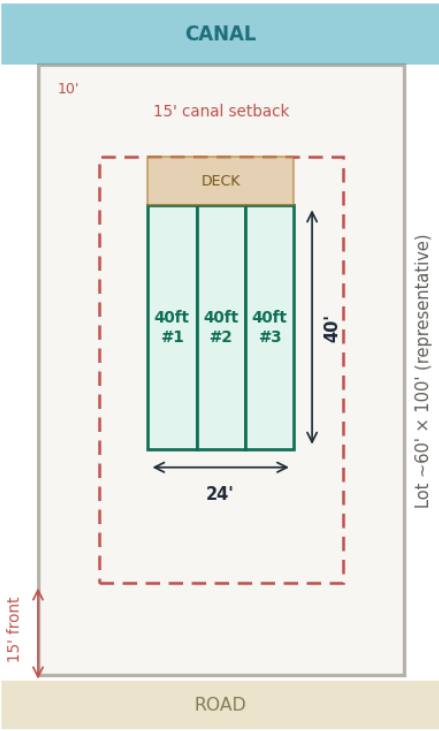

**Option B — two level, 2 × 40ft per floor**  
1,280 sq ft · 3 bed / 2 bath · 16' × 40' footprint

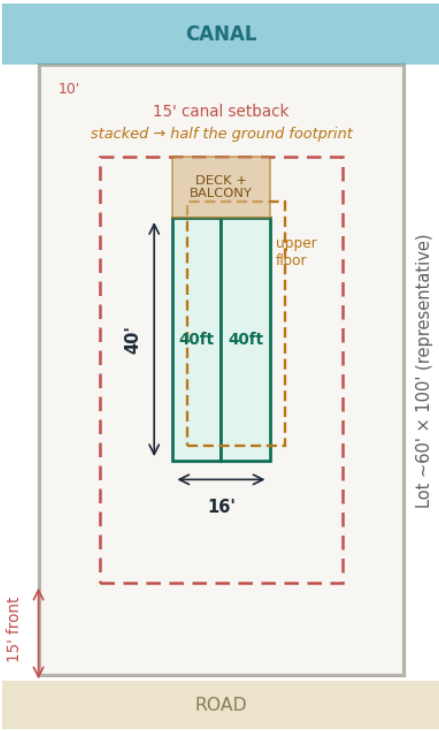

**Option C — Pacific Bin style, 5 × 40ft**  
1,600 sq ft · 3 bed / 1.5 bath · two level

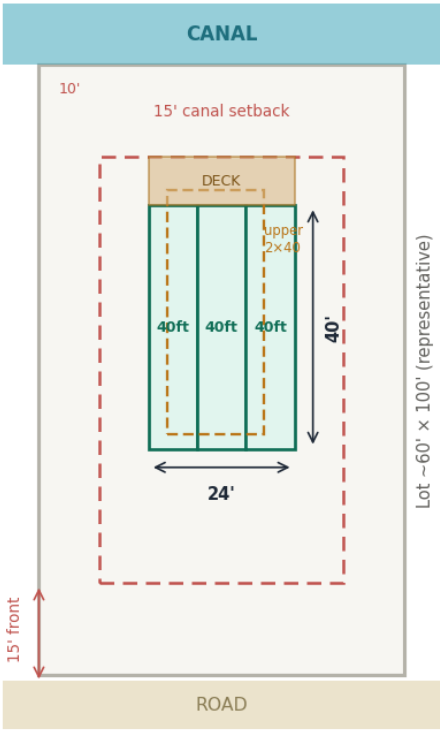

Lot size representative — replace with surveyed #207/#208 dimensions. Setbacks per Moonlight Bay covenant (15' front, 10' sides). Container = 40ft high-cube: 8' wide × 40' long × 9'6" tall. Footprint = container floor only; decks/stairs extend beyond.

### Procurement & landed cost (companion files):

- **Supplier spec & questions sheet** — issue to both factories with Sheet B001; asks for V2 base, V3 increment, and site alternates on one four-module base, DDP to 240-A Bayview Drive.
- **Landed-cost worksheet** — enter each supplier's three figures plus freight, duty (HS 9406.20), inland trucking, crane, and foundation to get per-unit landed cost and resale margin.
- **Tracker site map** — live lot statuses with #207/#208 and mound sites marked; use to confirm lot availability and the orientation finding above.

These companion files are delivered alongside this master. The schematic package (14 sheets) follows immediately after this page, reproduced without alteration.

# Two homes. One coastal building platform.

Design brief and schematic architectural drawings for factory coordination | Assumed Belize project context

## Design direction

Two stacked pairs of 40-foot high-cube containers create a compact two-story villa. Broad end glazing frames beach and canal views; independent decks extend both ends. Pale exterior finishes, a shaded roof and warm soffits soften the industrial structure.

## Two-bedroom villa / V2

Two upper bedrooms and two shared bathrooms total. The lower canal end stays open as a dining / work lounge, giving the living floor views in both directions. Best for a couple, a small family or longer stays.

## Three-bedroom villa / V3

Two upper bedrooms plus an enclosed lower guest bedroom. Two shared bathrooms total. The lower guest room overlooks the canal; living, dining and kitchen face the beach. Same module footprint and upper plan as V2.

## What this package authorizes

Use for design review, coordinated engineering development and comparable factory quotations. It does not authorize container cutting, steel procurement or construction. The responsible local architect / engineer must develop and approve the site-specific construction set.

| Measure                   | Both V2 and V3                                |
|---------------------------|-----------------------------------------------|
| Containers                | 4 x 40 ft high cube; 2 per level              |
| External main footprint   | 4,876 x 12,192 (16 x 40 ft nominal)           |
| Gross shell area          | 118.90 m2 / 1,280 ft2 over two levels         |
| Approx. net planning area | About 98 m2 / 1,057 ft2; see G002             |
| Outdoor decks / balconies | 40.96 m2 total across both levels             |
| Main floor levels         | Lower +/-0; upper +3,048 (provisional)        |
| Reference style           | Pacific Bin / two-level coastal villa         |
| Issue status              | Schematic Rev 01; no engineering calculations |

**Read first:** no survey, covenant, geotechnical report or flood datum was supplied. Lot numbers 207/208 and Moonlight Bay appear only in the research narrative. This package does not establish that either house fits those lots.

Package: basis + siting (G002-G003); four floor plans (A101-A202); elevations (A301-A302); section (A401); structural coordination (S001); openings (A501); factory scope (B001); sources and decisions (G004).

# Design basis, area and dimensional control

External module geometry is fixed for planning; finished geometry remains a factory coordination item

| Item                        | Planning basis                          | Verification required                                              |
|-----------------------------|-----------------------------------------|--------------------------------------------------------------------|
| 40 ft high-cube shell       | 12,192 L x 2,438 W x 2,896 H            | Measure chosen stock and corner castings before shop drawings      |
| Example unlined interior    | About 12,032 L x 2,350 W x 2,700 H      | Fleet dimensions vary; supplier data governs [1]                   |
| Perimeter allowance         | 200 each side from exterior face        | Includes shell + lining provision; not an insulation specification |
| Internal partitions         | 100 nominal                             | Confirm fire, acoustic, wet-area and service build-ups             |
| Finished ceiling target     | At least 2,400 clear in habitable rooms | Coordinate insulation, beams, ducts and local minimums             |
| Main finished floors        | 0 / +3,048 provisional                  | 2,896 shell plus 152 interface / floor-zone allowance              |
| Gross shell floor area      | 4 x 12.192 x 2.438 = 118.90 m2          | 1,280 ft2 nominal; decks excluded                                  |
| Interior-envelope estimate  | 2 x 4.476 x 11.792 = 105.56 m2          | Before partitions, seam columns and stair opening                  |
| Net planning estimate       | 105.56 - 7.40 = 98.16 m2                | Approx. 1,057 ft2; not certified usable/covenant area              |
| Three-container alternative | 89.17 m2 / 960 ft2 gross                | Below a 1,000 ft2 minimum, if that covenant is confirmed           |

## Area assumptions


Net estimate deducts one upper stair void (about 4.7 m2) and about 2.7 m2 of partitions (conservative V3 allowance). Structural posts, shafts and final finishes may reduce it further. Require an architect-certified schedule using the covenant definition before claiming compliance.

## Dimension convention

Floor-plan dimensions locate schematic zones and outer shell faces. Room sizes are approximate clear envelopes, not guaranteed finish dimensions. No dimensions should be scaled from screenshots. Print PDF at 100% on A3 for the stated floor-plan scale.

# Beach / canal siting strategy

Relationship diagram only - no surveyed lot boundary, cardinal north or setback distances established

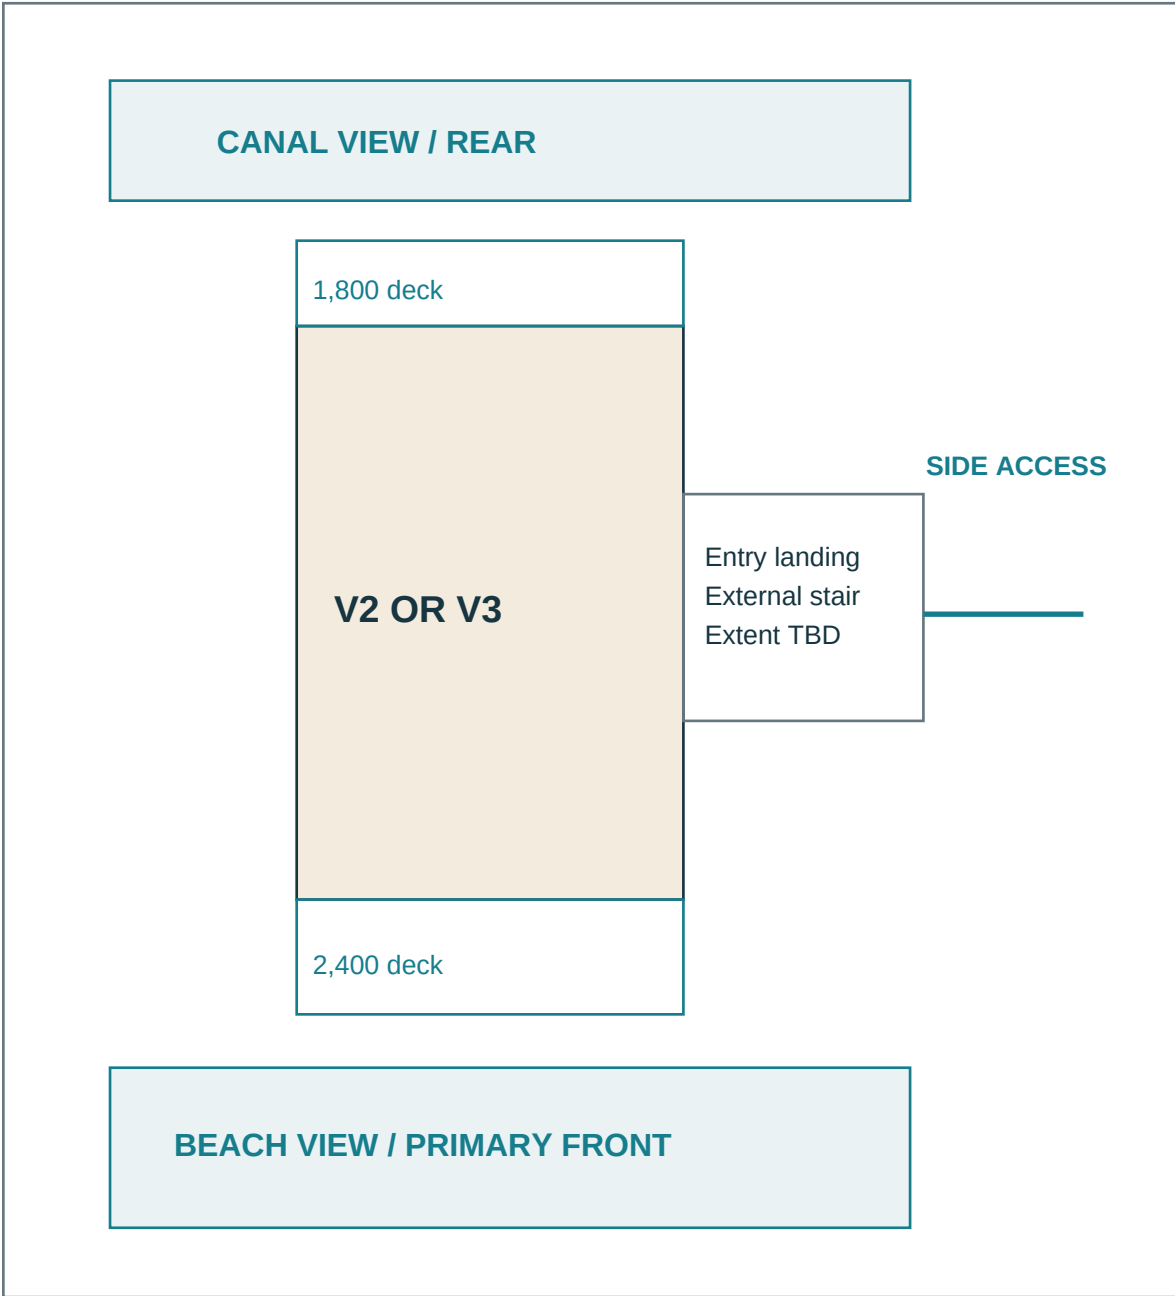

Dashed/survey boundaries are intentionally not invented. Diagram is not a site plan.

## Assumed view arrangement

Beach and canal lie at opposite short ends of the home. Confirm with the actual survey and photographs. If the water views are adjacent, rotate the home or develop corner glazing after structural review; do not mirror blindly.

## Envelope to test against the survey

Main shell: 4,876 x 12,192. Deck-to-deck envelope: 4,876 x 16,392, excluding posts, eaves, side entry and external stairs. Allow separate space for access, drainage, utilities and crane outriggers.

## Elevated coastal foundation

Set the lower occupied floor from the adopted flood / surge criterion and required freeboard. Obtain geotechnical and scour advice. Keep the undercroft open unless the local engineer approves an alternative. No foundation depth or pile size is established here.

## Site design work before layout freeze


Locate both water edges, legal boundaries, easements, setbacks, road and utility connections, septic / sewer constraints, prevailing winds and solar exposure. Confirm two-story and height rules, including how elevated floors are counted.

## Access and resilience

Develop the exterior stair from actual finished grade to the side entry at lower level. Provide landings, guards, lighting and slip-resistant finishes. Confirm an accessible route if required by the intended occupancy. Keep outdoor equipment above the design flood level.

# V2 / lower floor

Dimensioned schematic | 1:75 at A3, 100% print | Beach at bottom; canal at top | Shell 4,876 x 12,192

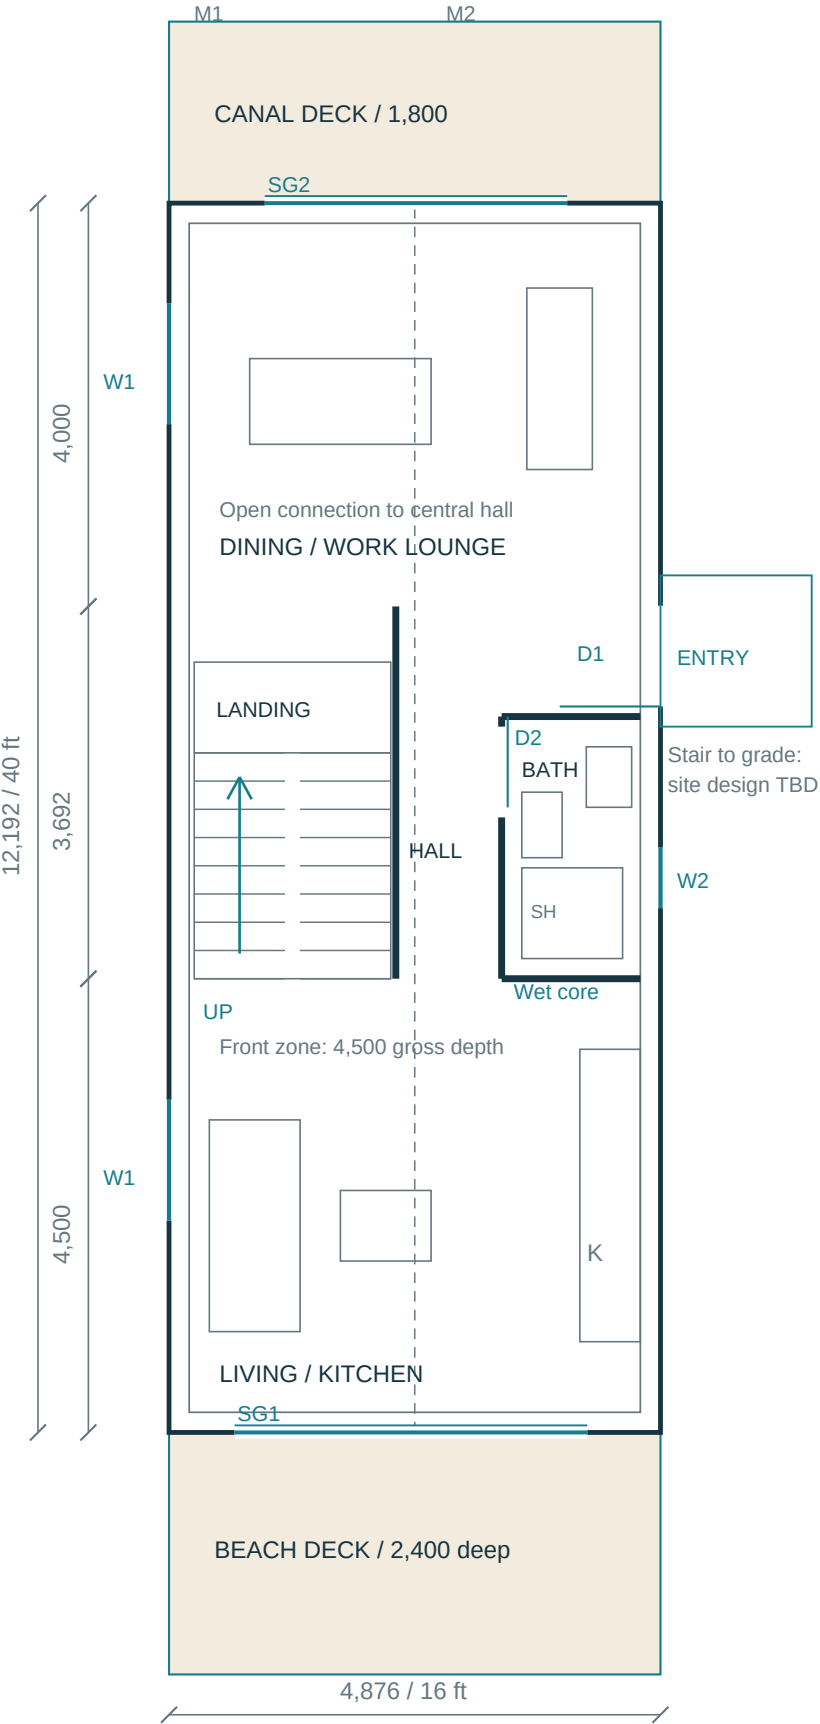

## Plan intent

The canal lounge remains open, with dining and workspace separate from the beach living area. A central full bath serves this floor.

## Structure and module junction

Dashed centerline marks the original container sidewall seam at x = 2,438. Removing walls to join rooms requires engineered transfer frames. Keep corner posts. Final steel may reduce the usable width or change this plan.

## Stair reservation

U-stair bay about 1,950 x 3,140 with two 900-wide flights. Preliminary geometry: 18 equal risers at about 169.3; 8 goings of 280 per flight; 900 intermediate landing. Dimensions are planning targets, not code approval. Engineer must check finished clear widths, handrails, upper opening and headroom.

## Room dimensions and doors

Bedroom sizes allow 200 perimeter lining and 100 partitions; columns and wardrobes are excluded. Internal hinged doors are 900 nominal openings. Bathroom D2 is a 900 nominal pocket opening. Drawn arcs show swing intent; hardware and actual clear openings remain to be coordinated.

## Exterior and services


SG1 / SG2 are glazed sliding assemblies. W1 is an operable bedroom escape-window candidate; net clear opening must be locally verified. Bath and kitchen service routes go to the central/east wet core. Add screened ventilation, dehumidification and outdoor equipment access.

Scale check: 5,000 mm = 66.67 mm on paper



# V2 / upper floor

Dimensioned schematic | 1:75 at A3, 100% print | Beach at bottom; canal at top | Shell 4,876 x 12,192

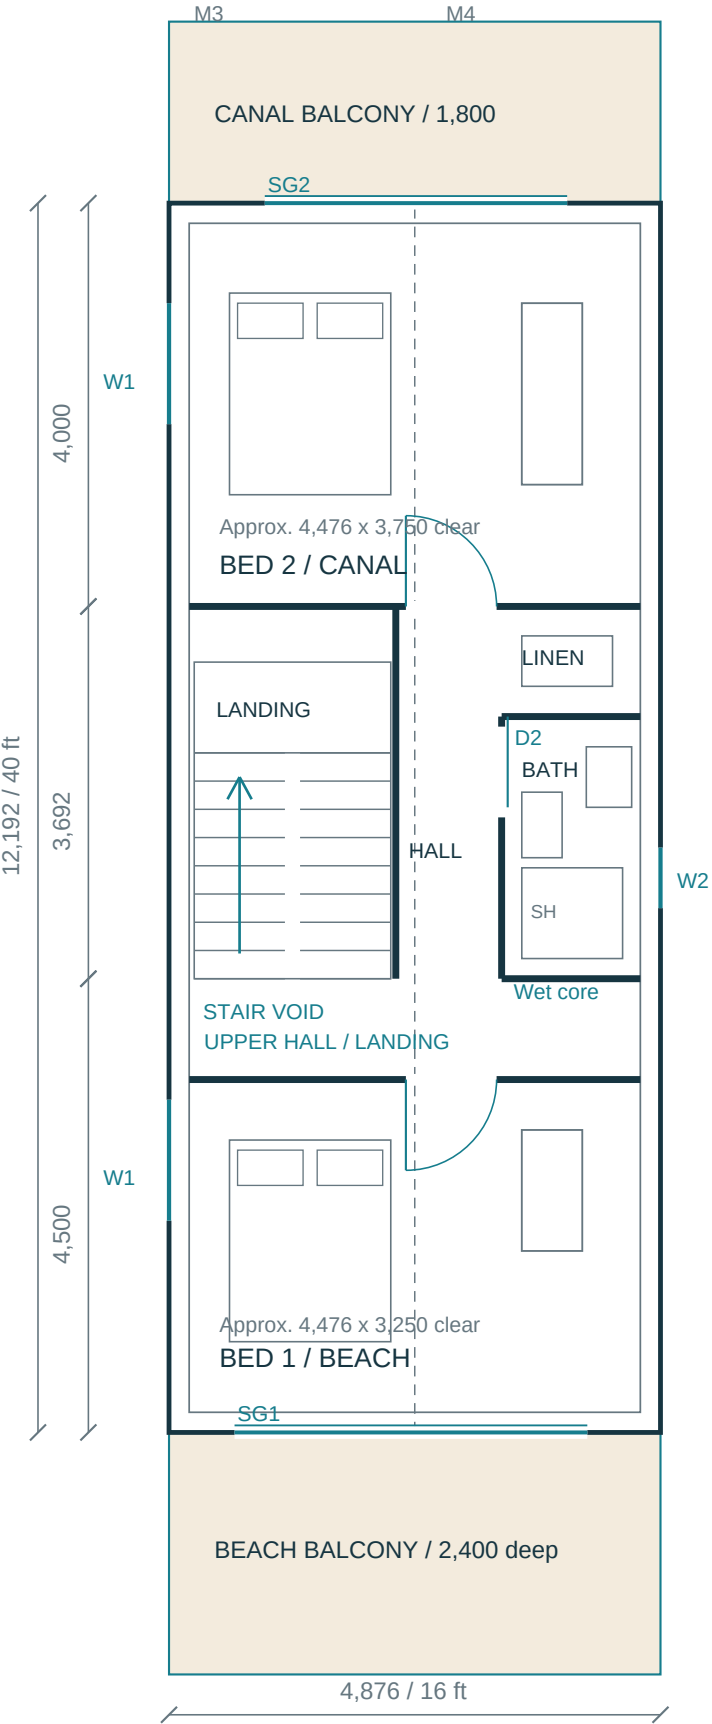

## Plan intent

Two upper bedrooms share a central shower bathroom. Each opens onto a water-facing balcony. A 1,000-deep upper landing occupies the south end of the stair, so Bed 1 ends at y = 3,500 within the 4,500 front zone. This upper layout is identical in both models.

## Structure and module junction

Dashed centerline marks the original container sidewall seam at x = 2,438. Removing walls to join rooms requires engineered transfer frames. Keep corner posts. Final steel may reduce the usable width or change this plan.

## Stair reservation

U-stair bay about 1,950 x 3,140 with two 900-wide flights. Preliminary geometry: 18 equal risers at about 169.3; 8 goings of 280 per flight; 900 intermediate landing. Dimensions are planning targets, not code approval. Engineer must check finished clear widths, handrails, upper opening and headroom.

## Room dimensions and doors

Bedroom sizes allow 200 perimeter lining and 100 partitions; columns and wardrobes are excluded. Internal hinged doors are 900 nominal openings. Bathroom D2 is a 900 nominal pocket opening. Drawn arcs show swing intent; hardware and actual clear openings remain to be coordinated.

## Exterior and services


SG1 / SG2 are glazed sliding assemblies. W1 is an operable bedroom escape-window candidate; net clear opening must be locally verified. Bath and kitchen service routes go to the central/east wet core. Add screened ventilation, dehumidification and outdoor equipment access.

Scale check: 5,000 mm = 66.67 mm on paper



# V3 / lower floor

Dimensioned schematic | 1:75 at A3, 100% print | Beach at bottom; canal at top | Shell 4,876 x 12,192

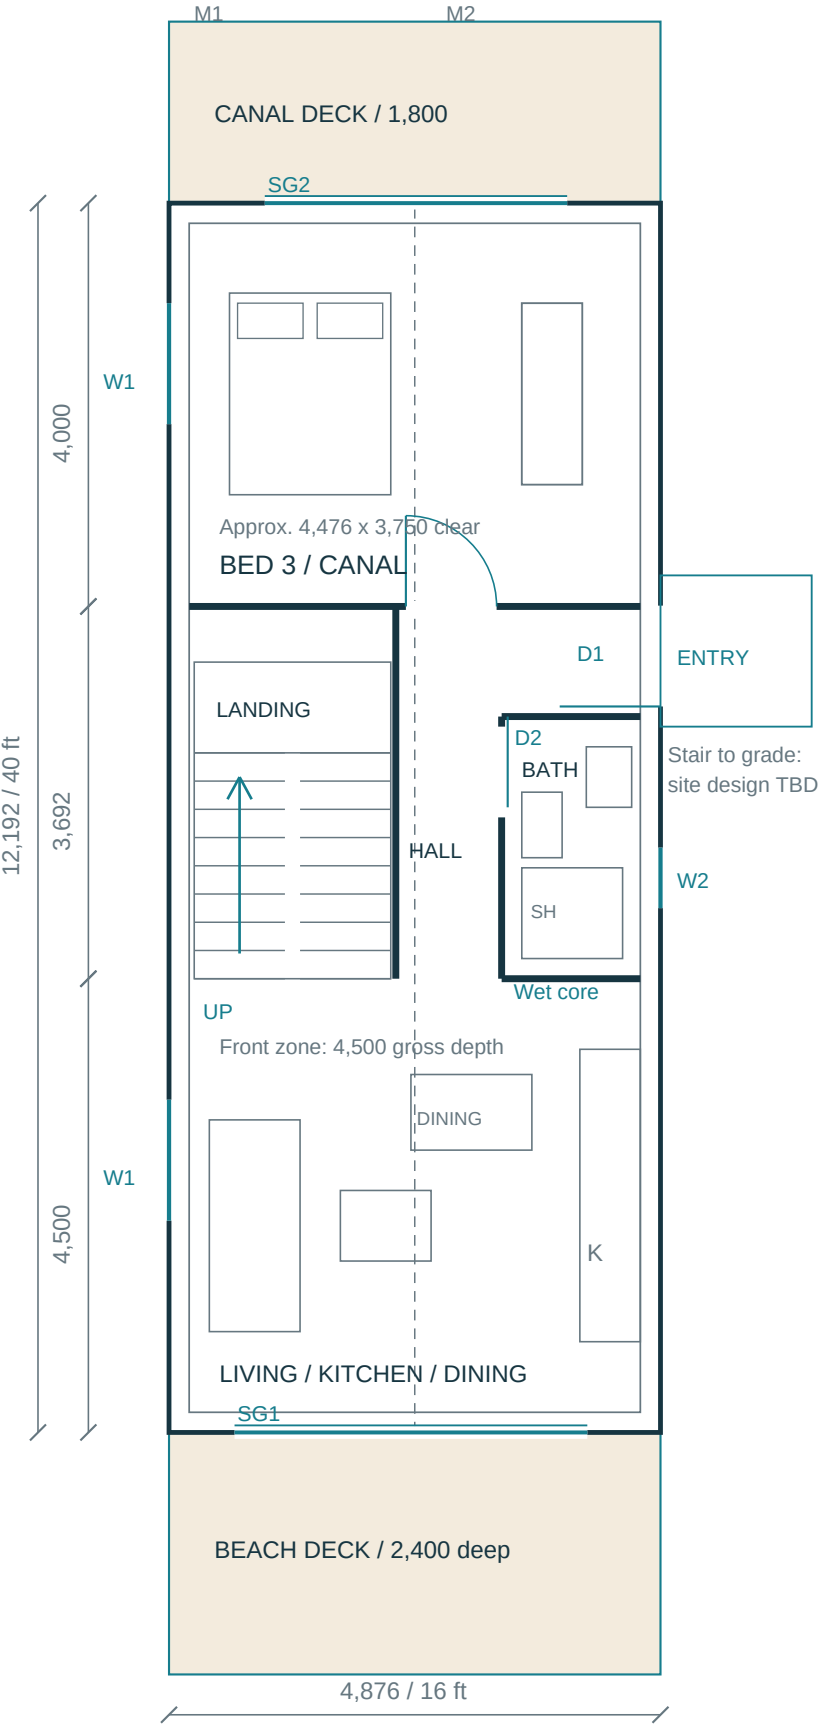

## Plan intent

An enclosed guest bedroom replaces the canal lounge. Dining moves into the beach living / kitchen zone. A central full bath serves guests and daytime use.

## Structure and module junction

Dashed centerline marks the original container sidewall seam at x = 2,438. Removing walls to join rooms requires engineered transfer frames. Keep corner posts. Final steel may reduce the usable width or change this plan.

## Stair reservation

U-stair bay about 1,950 x 3,140 with two 900-wide flights. Preliminary geometry: 18 equal risers at about 169.3; 8 goings of 280 per flight; 900 intermediate landing. Dimensions are planning targets, not code approval. Engineer must check finished clear widths, handrails, upper opening and headroom.

## Room dimensions and doors

Bedroom sizes allow 200 perimeter lining and 100 partitions; columns and wardrobes are excluded. Internal hinged doors are 900 nominal openings. Bathroom D2 is a 900 nominal pocket opening. Drawn arcs show swing intent; hardware and actual clear openings remain to be coordinated.

## Exterior and services


SG1 / SG2 are glazed sliding assemblies. W1 is an operable bedroom escape-window candidate; net clear opening must be locally verified. Bath and kitchen service routes go to the central/east wet core. Add screened ventilation, dehumidification and outdoor equipment access.

Scale check: 5,000 mm = 66.67 mm on paper



# V3 / upper floor

Dimensioned schematic | 1:75 at A3, 100% print | Beach at bottom; canal at top | Shell 4,876 x 12,192

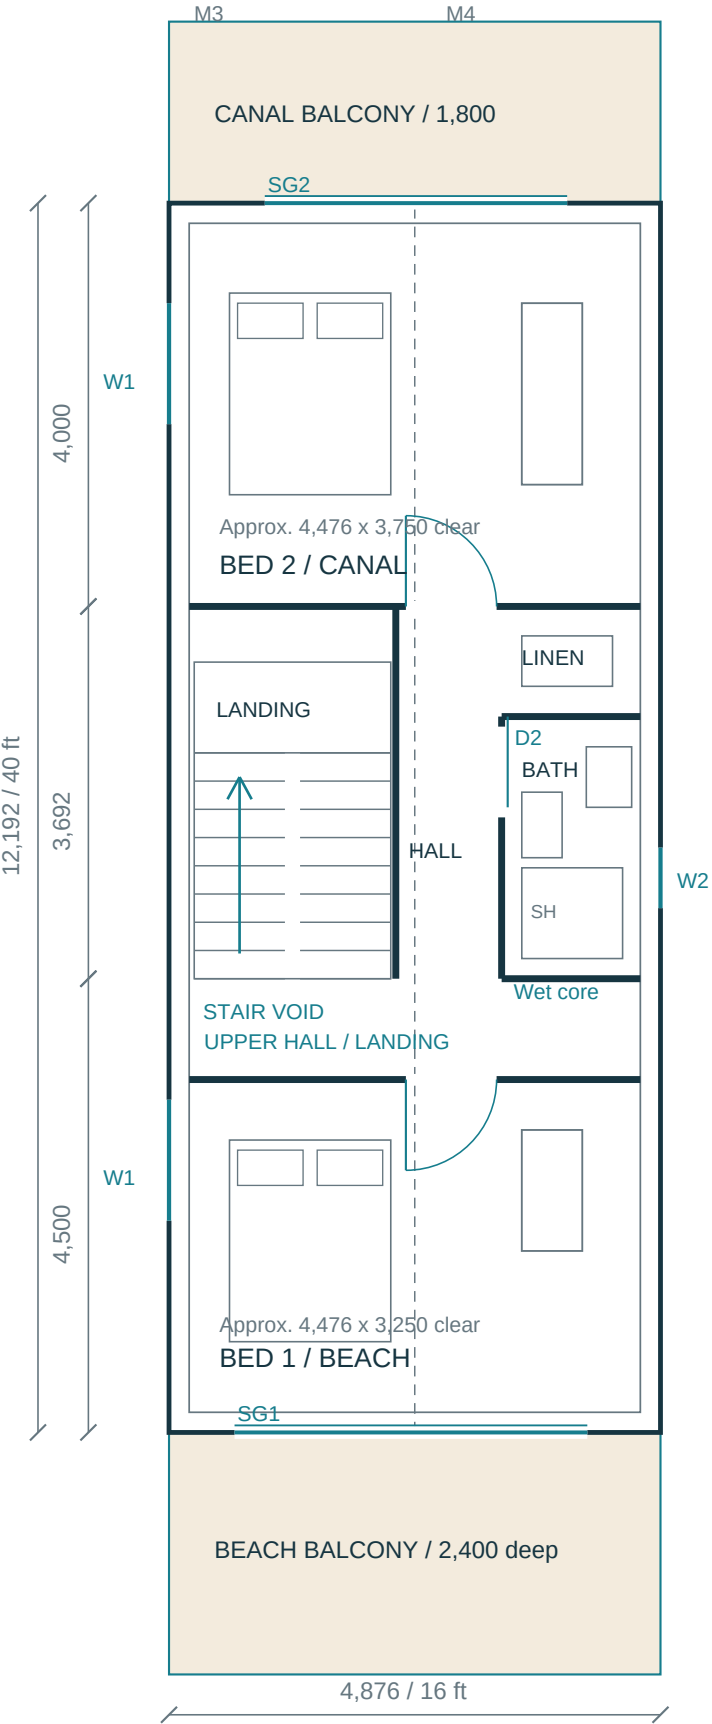

## Plan intent

Two upper bedrooms share a central shower bathroom. Each opens onto a water-facing balcony. A 1,000-deep upper landing occupies the south end of the stair, so Bed 1 ends at y = 3,500 within the 4,500 front zone. This upper layout is identical in both models.

## Structure and module junction

Dashed centerline marks the original container sidewall seam at x = 2,438. Removing walls to join rooms requires engineered transfer frames. Keep corner posts. Final steel may reduce the usable width or change this plan.

## Stair reservation

U-stair bay about 1,950 x 3,140 with two 900-wide flights. Preliminary geometry: 18 equal risers at about 169.3; 8 goings of 280 per flight; 900 intermediate landing. Dimensions are planning targets, not code approval. Engineer must check finished clear widths, handrails, upper opening and headroom.

## Room dimensions and doors

Bedroom sizes allow 200 perimeter lining and 100 partitions; columns and wardrobes are excluded. Internal hinged doors are 900 nominal openings. Bathroom D2 is a 900 nominal pocket opening. Drawn arcs show swing intent; hardware and actual clear openings remain to be coordinated.

## Exterior and services

SG1 / SG2 are glazed sliding assemblies. W1 is an operable bedroom escape-window candidate; net clear opening must be locally verified. Bath and kitchen service routes go to the central/east wet core. Add screened ventilation, dehumidification and outdoor equipment access.


Scale check: 5,000 mm = 66.67 mm on paper



# Beach and canal elevations

Shared architectural envelope for V2 and V3 | Orthographic concept; elevations NTS


BEACH / SG1

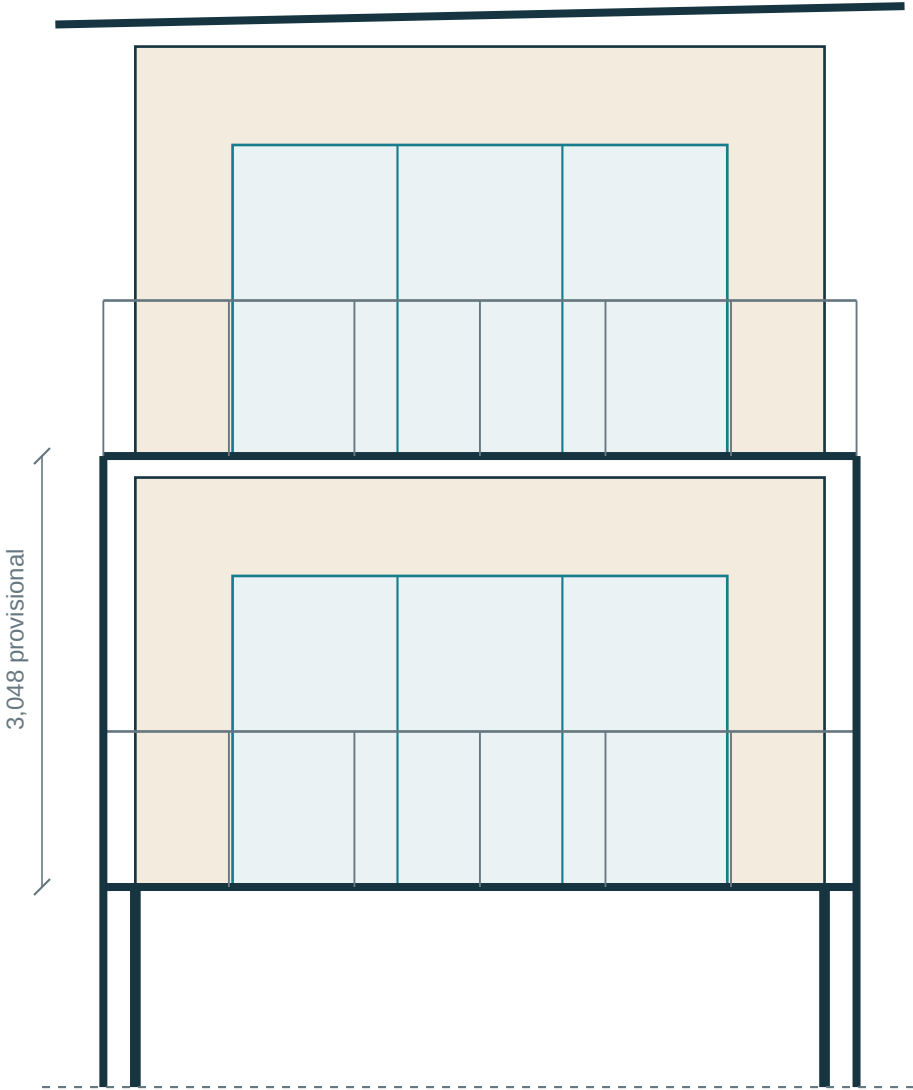

ILLUSTRATIVE GRADE - HEIGHT TBD

**Material intent:** light warm-grey marine exposure coating; compatible insulated rainscreen where used; timber-look ventilated soffits; pale slip-resistant decking; screened operable windows. Coastal coating system, metal compatibility and maintenance schedule require supplier / engineer approval.

CANAL / SG2

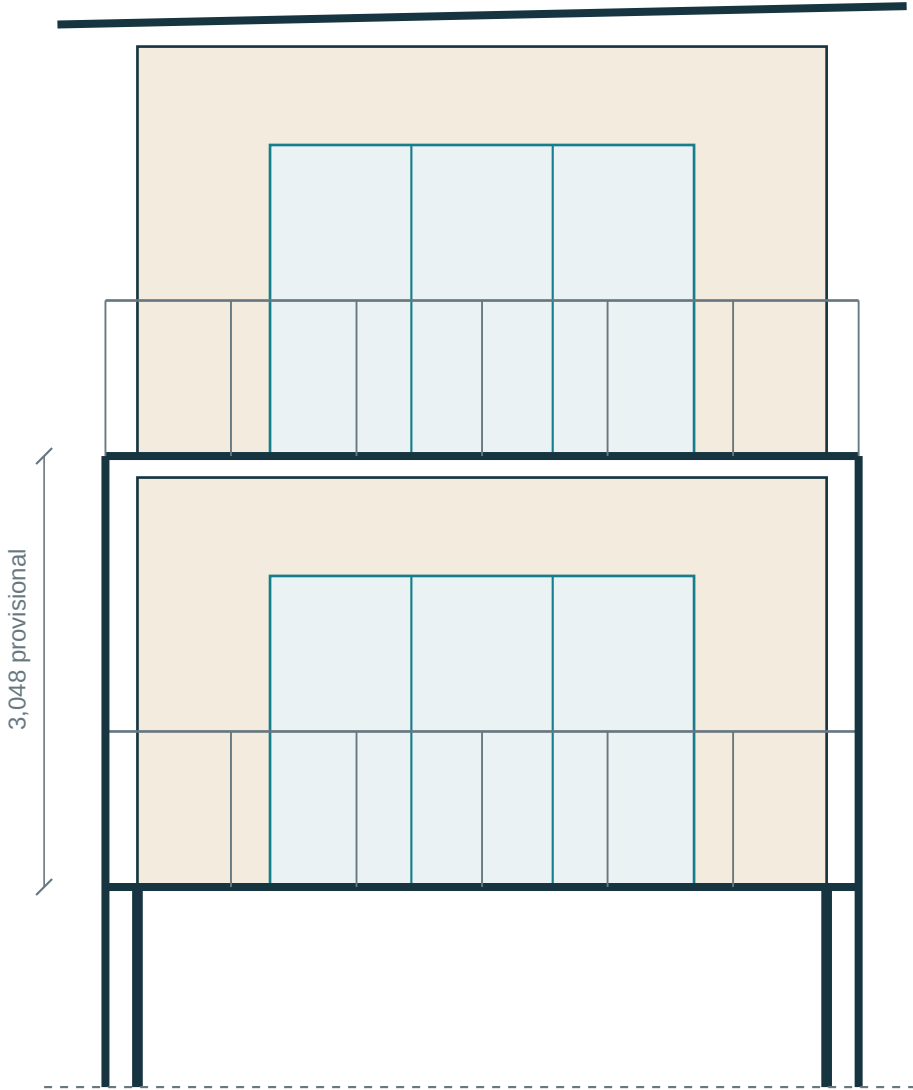


ILLUSTRATIVE GRADE - HEIGHT TBD

**View protection:** use slender engineered guard systems with locally compliant height and openings. Glazing must meet the project wind pressure and impact criteria where required. Sliding glass alone is not a hurricane-resistance specification. Screens and shading must also resist design wind.


# Side elevations and coastal roof intent

Shared form for V2 and V3 | Side 1 is entry / wet-core side; side 2 is opposite | NTS

ENTRY SIDE

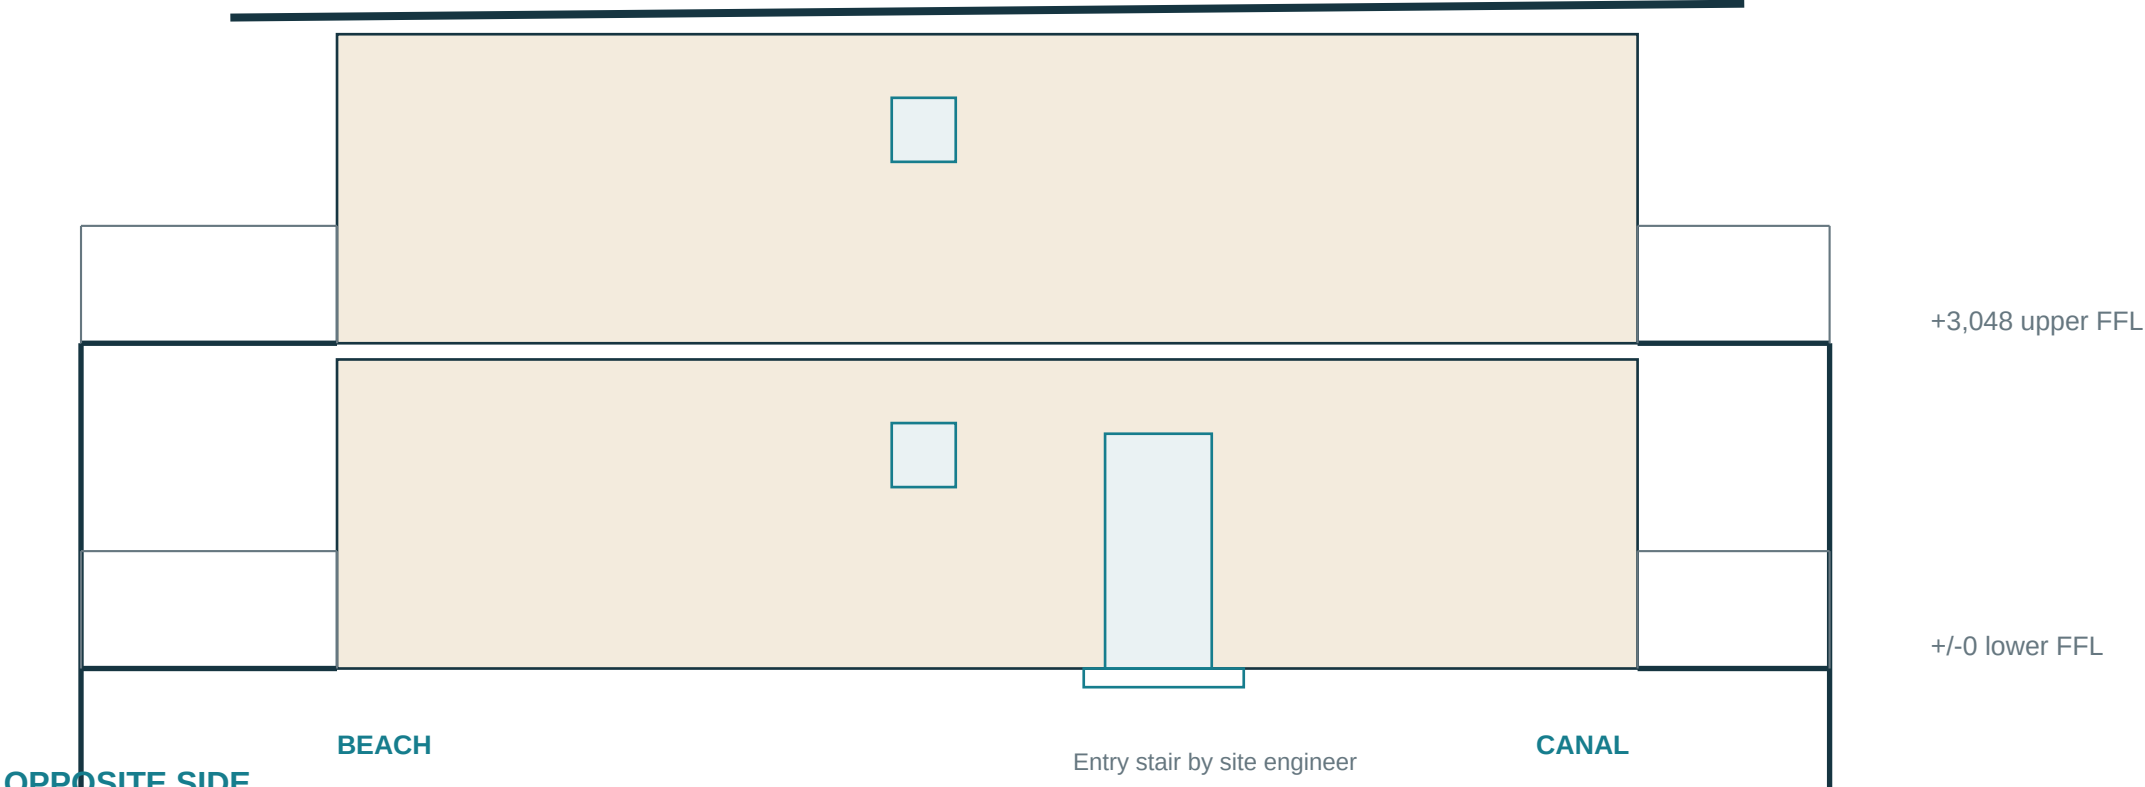

OPPOSITE SIDE

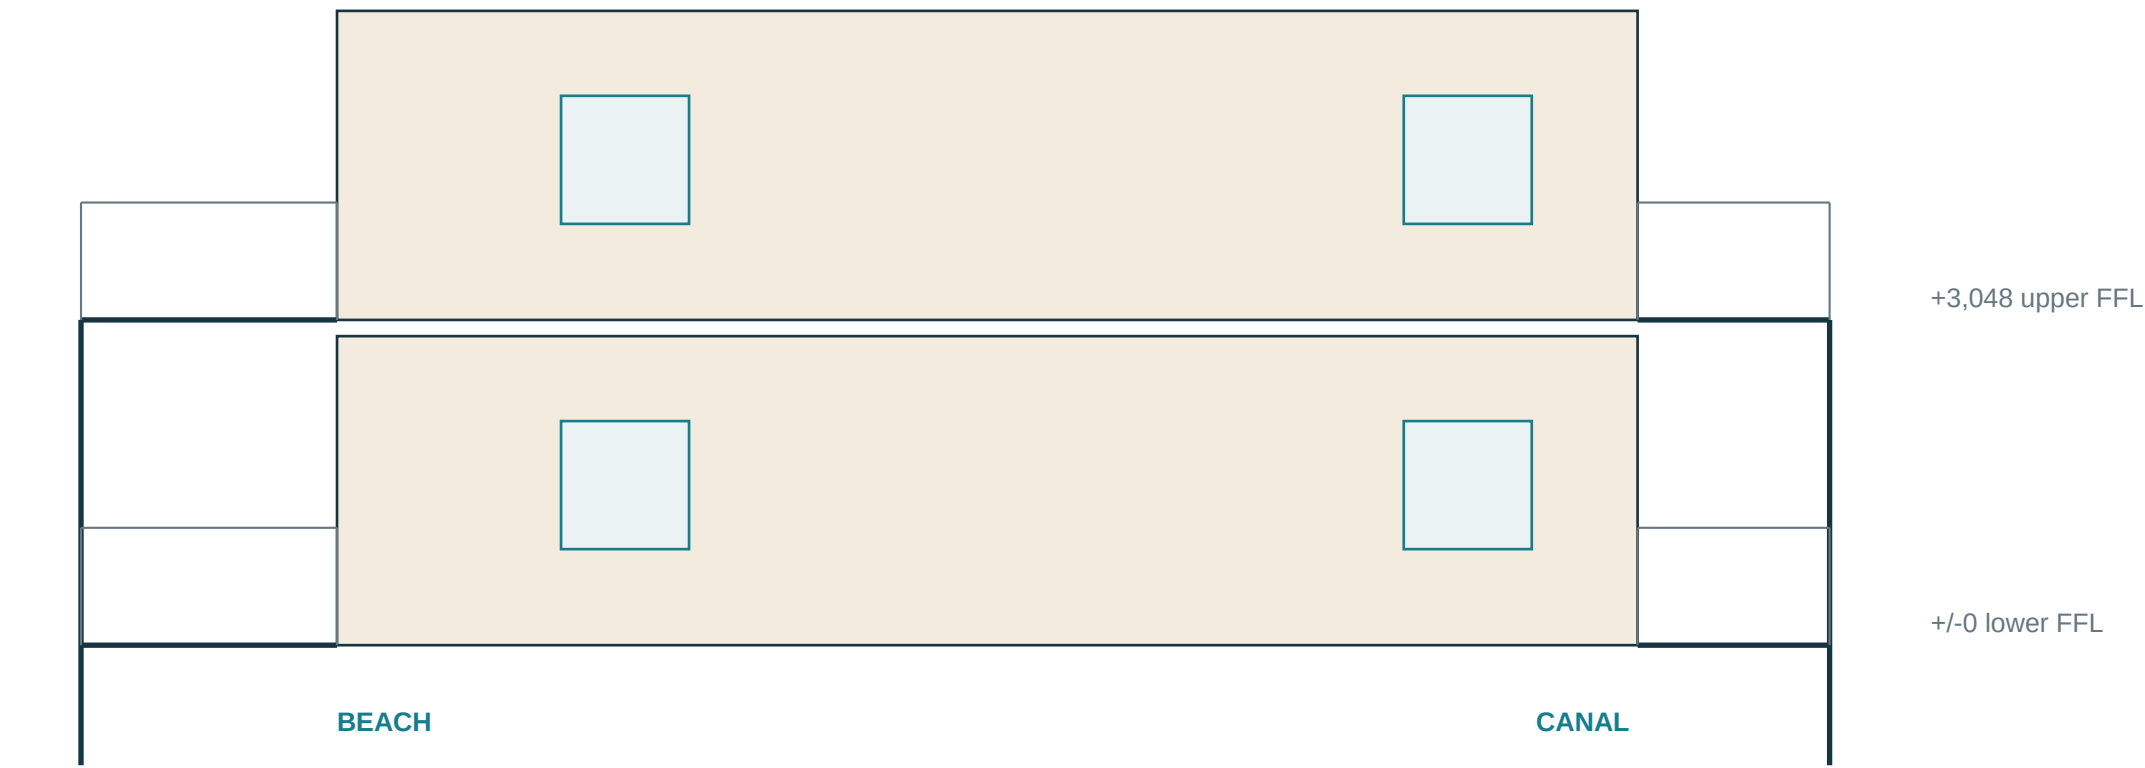


**Roof:** lightweight ventilated over-roof on engineered brackets; slope and drainage to be developed. Do not rely on flat container roofs for a finished waterproofing system.

**Canopies / decks:** concept depths shown on plans; members, foundations and uplift connections must be independently designed. No occupied roof terrace is included.

**Envelope:** preserve inspection and repainting access to seams, posts and concealed metal.

# Section through the stacked modules

Transverse envelope / load path and internal stair geometry | Diagrammatic; no structural sizes assigned

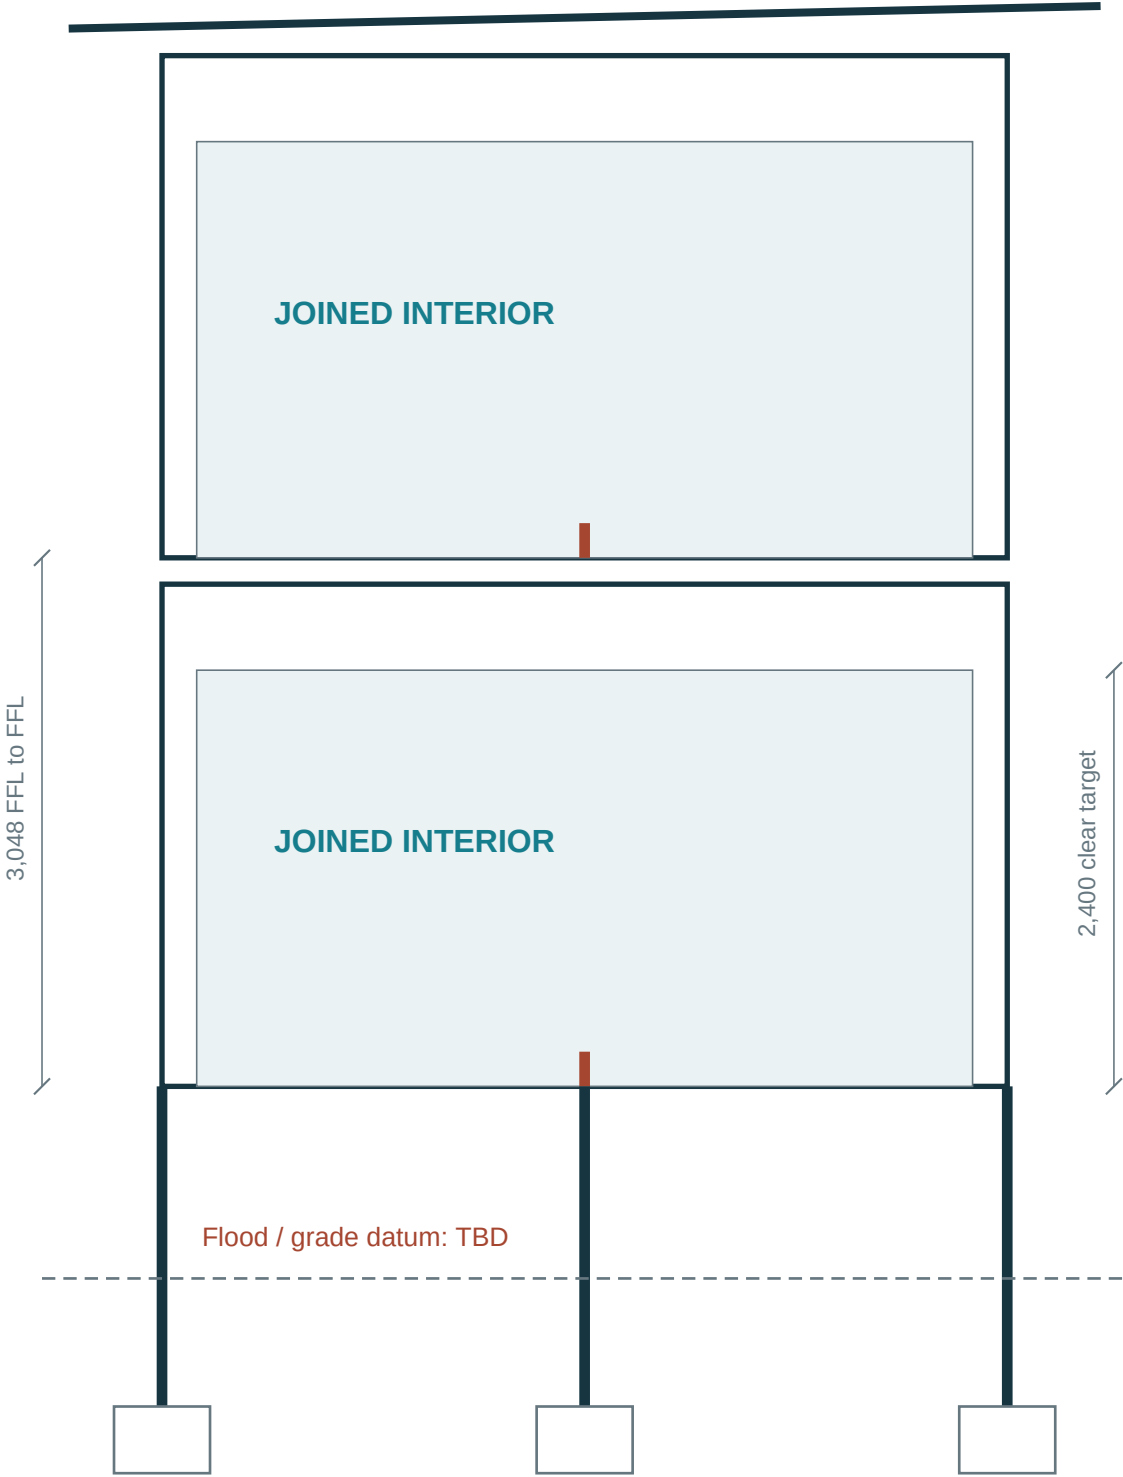

Foundation shapes show load-path intent only. No pile / footing type, depth, spacing or reinforcement is selected.

## Shell stack and finished heights

Upper shell is aligned over the lower shell. A provisional 152 interface zone reconciles a 2,896 high shell with the 3,048 finished-floor target. Factory must coordinate rails, connection plates, flooring and waterproofing; revise risers when the actual floor-to-floor height is frozen.

## Critical transfer condition

The center seam and removed sidewalls cannot be assumed to carry loads after cutting. Engineer replacement posts / beams for gravity and lateral forces, preserving a continuous roof-to-foundation load path. Added steel must be reflected in headroom and furniture clearances.

## Thermal and moisture control

Propose a continuous insulated envelope including the underside. Provide an assembly-specific condensation assessment for warm humid marine air and air-conditioned interiors. Maintain air / water barrier continuity across transport joints; do not prescribe a vapor barrier location without analysis.

## Stair headroom and opening

Reserve a U-shaped upper floor opening within the 1,950 x 3,140 stair bay, except the intermediate landing projection. Final trimmers, landing support, nosing-to-soffit clearance, guards and handrails are engineer / architect scope. No stair opening may be field-cut from this diagram.


## Coastal substructure

Determine flood / surge / wave and scour conditions, geotechnical bearing and lateral resistance. Design piles or other foundations and container hold-downs for those conditions. Utility connections need accessible isolation and movement allowance.

# Factory structural coordination map

Engineering brief only | Retain corner posts; the original container load rating is not a building design

4 x 40 ft HC / aligned stack

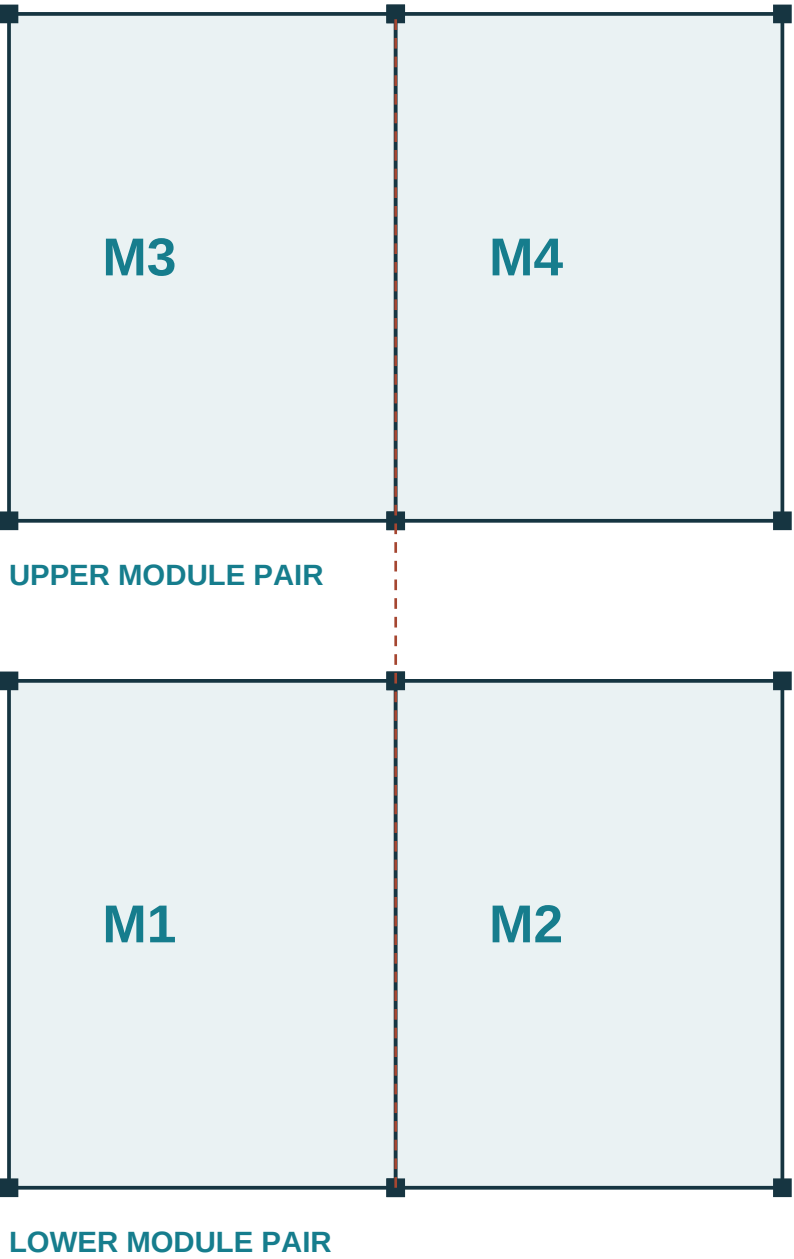

Solid squares: retained corner castings / posts. Red dashed line: joined sidewalls requiring engineered replacement frames. Final support points are not limited to the squares.

## S1 / Analysis and structural basis

Submit local code / standard basis, design loads and combinations, wind exposure and enclosure classification, seismic basis where applicable, flood actions, corrosion allowances and deflection criteria. Include altered-container analysis, floor capacity, roof diaphragm and lateral bracing.

## S2 / Openings and replacement steel

Mark exact wall cut limits for SG1, SG2, W1, W2, entry doors, internal seams and the stair void. Design header / jamb frames, seam columns, trimmers and connections. Provide opening tolerances and a no-cut zone plan. Factory must flag conflicts with the 2,400 clear-height target.

## S3 / Connections and temporary works

Engineer inter-module ties, foundation anchors, deck interfaces and roof fasteners for shear and uplift. Issue weld / bolt schedules and inspection requirements. Analyze lifting, transport, temporary bracing and erection stability after shell modification; define lift points and module weights.

## S4 / Durability and traceability

Inspect shell grade, thickness, corrosion, repairs, cargo history and floor condition. Propose one-trip shells or a documented equivalent. Provide coating preparation, compatible primer / intermediate / topcoat system, dry-film-thickness targets and repair procedure; isolate dissimilar metals.

## S5 / Fabrication release gate

Release only after approved engineering calculations, site reactions and foundations, coordinated shop drawings, MEP penetrations and shipping dimensions are accepted by the responsible project professionals. Establish a trial assembly and dimensional survey before finishing.

# Openings and coordination schedule

Nominal architectural openings, not cut-out sizes | Counts correspond to these four floor plans

| Tag | Nominal W x H | Location / quantities per villa         | Design requirement                                                                        |
|-----|---------------|-----------------------------------------|-------------------------------------------------------------------------------------------|
| SG1 | 3,500 x 2,200 | Beach: 1 lower + 1 upper; both models   | Sliding assembly; engineer jamb/header; safety glass and wind / impact rating as required |
| SG2 | 3,000 x 2,200 | Canal: 1 lower + 1 upper; both models   | Sliding assembly; drained sill, accessible maintenance and wind rating                    |
| W1  | 1,200 x 1,200 | Opposite side: 2 lower + 2 upper        | Nominal sill 900; operable. Bedroom net clear escape opening and sill to be verified      |
| W2  | 600 x 600     | Entry side: 1 bathroom per floor        | Nominal sill 1,700; privacy glass; screened operable or mechanical exhaust                |
| D1  | 1,000 x 2,200 | Lower side entry: 1 per villa           | Weather-sealed exterior door; landing, swing and clear width coordinated                  |
| D2  | 900 x 2,100   | Bathroom pocket door: 2 per villa       | Provide full pocket frame / service-free wall; verify clear passage and privacy latch     |
| D3  | 900 x 2,100   | Upper bedroom doors: 2; V3 adds 1 lower | Hinged inward; resolve furniture and wardrobe conflicts before release                    |

## Door references

Plan arcs without a tag are D3. Nominal widths represent architectural intent and may differ from required rough openings. Obtain manufacturer shop drawings before sizing structural openings.

## Guards and glazing

Use a 1,100 high guard as a preliminary design target only. Local architect must determine actual height, opening limitations and design loads. Glass guards require their own engineering and compatible corrosion-resistant fixings.

## MEP coordination

Stack bathroom services at the entry-side core. Kitchen occupies the lower beach-side wall; route drainage to the core without cutting structural rails. Reserve an accessible service riser, water heater / laundry cabinet and shutoffs in coordinated casework; exact sizes remain open.

## Space coordination hold

Final mechanical equipment, electrical panel, laundry, water heater and service shafts are not fully drawn. Factory must return a coordinated fit study before plan approval. This may adjust cabinetry, bath partitions or room clear areas.

# Factory design brief and quotation scope

Request comparable V2 and V3 proposals on the same four-module base; list every exclusion

| Work package        | Factory to provide                                                                                 | Local / site design responsibility                                                    |
|---------------------|----------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Architecture        | Coordinated dimensioned plans; four elevations; sections; room / area schedule; material samples   | Survey placement; covenant / planning review; occupancy and accessibility basis       |
| Structure           | Altered-shell calculations; shop drawings; welds / bolts; lifts; weights; interface loads          | Local review; foundation / flood / geotechnical design; complete load-path acceptance |
| Envelope            | Roof and joint details; glazing ratings; coating system; insulation / condensation strategy        | Confirm climate and hazard criteria; installation inspection                          |
| MEP                 | Load schedules; circuit / plumbing diagrams; equipment cut sheets; wet-area details                | Utility availability and voltage / frequency; local approvals; sewer / septic design  |
| Delivery / erection | Packing list; module dimensions and mass; lift plan; assembly sequence; repair kits                | Road / port route; crane pad and access; site erection and utility connections        |
| Quality / handover  | Trial fit; water tests; electrical / plumbing tests; coating and weld records; as-builts; warranty | Inspection / acceptance; occupancy approval; owner maintenance plan                   |

## Require three separately priced figures

- 1. Base V2 with two bedrooms and two bathrooms.
- 2. Increment to V3: rear bedroom partition, door and wardrobe; dining relocation.
- 3. Site-supplied scope: foundations, four decks / balconies, exterior stair, crane, utility works, freight, duties and commissioning. Factory may price these as separate alternates.

## Quote schedule

State currency, validity, Incoterm and named place, taxes, lead time after approved drawings, engineering fees, payment milestones, shipping volume / mass, erection duration, warranty and all exclusions. Identify whether the product is a converted ISO container or a purpose-built steel module.

**Factory return package:** PDF review set + editable DWG/DXF or IFC/Revit model + calculations + coordinated specification + priced inclusions/exclusions. This concept package supplies editable vector sheets and a millimeter DXF floor-plan basis; it does not supply engineered shop drawings.

# Inputs to resolve and source register

Use this page as the agenda for the first owner / factory / local engineer coordination meeting

| Priority | Decision / missing input                                                                     | Owner                           |
|----------|----------------------------------------------------------------------------------------------|---------------------------------|
| 1        | Survey for lots 207/208; legal setbacks / easements; exact beach and canal directions        | Owner + surveyor                |
| 1        | Actual covenant text: minimum floor-area definition; stories / height; exterior restrictions | Owner + local architect         |
| 1        | Flood / surge / wave criteria, freeboard, geotechnical and scour data                        | Local engineer                  |
| 1        | Container system: true 40 ft HC conversions or different factory module dimensions           | Factory                         |
| 2        | Private home vs rental / resort occupancy; accessibility and fire requirements               | Owner + local architect         |
| 2        | Choose V2 or V3; two shared baths vs requested ensuite alternative                           | Owner                           |
| 2        | Utility voltage / frequency, water / sewer, HVAC, laundry and hot-water equipment            | Factory + local MEP             |
| 2        | Finished stair geometry, final steel intrusion, ceiling height and certified usable area     | Architect + structural engineer |
| 3        | Material palette, glazing supplier, coating warranty, budget and delivery programme          | Owner + factory                 |

## SOURCE REGISTER / reviewed 07 September 2026

- [1] Hapag-Lloyd: 40 ft Standard High Cube. Example interior dimensions; manufacturer variation explicitly noted.
- [2] Belize CBA: Procedures for Building Unit. Local architectural / structural responsibility and submission process.
- [3] FEMA Technical Bulletin 8: Corrosion Protection for Metal Connectors and Fasteners in Coastal Areas. Reference link; full PDF could not be retrieved. Not Belize code.
- [4] The Pacific Bin: construction-plan listing. Style / programme reference; purchased drawings were not supplied or reproduced.

Also reviewed: user-supplied Pasted markdown.md. Its statements about covenant compliance, plan licensing, lot geometry and prior delivered PDFs are unverified. The 960 ft2 / 1,000 ft2 contradiction is corrected in this package. Obtain commercial-use rights separately if adopting any third-party purchased plan.
